



# Renovation Progress

Oct. 4-14, 2011



**Oct. 4<sup>th</sup> Setting up the office & Moving Chapel A/C units to north side of the building**



**Oct. 5 Delivering equipment,  
moving chapel A/C connections,  
& sanding down buckled sidewalk  
in front of chapel for safer  
passage**





**Oct. 6- Safety fencing is set up, cones to direct guests to the monastery's temporary entrance in Annunciata Hall**



Oct. 7<sup>th</sup> – Arrival  
of more  
equipment and  
materials





**Oct. 7<sup>th</sup> Hand carrying materials to 2<sup>nd</sup> Otilia, protecting the Pergo floor**






**Oct 10<sup>th</sup> – The temporary  
monastery entrance and route  
to chapel**





**Oct. 11<sup>th</sup> – 1<sup>st</sup> Ottilia  
floor protection, tunnel  
construction, chasing  
down passageway  
electricity, removal of  
Ottilia steam heat valve,  
chunking the junk from  
3<sup>rd</sup> Ottilia out the  
window**

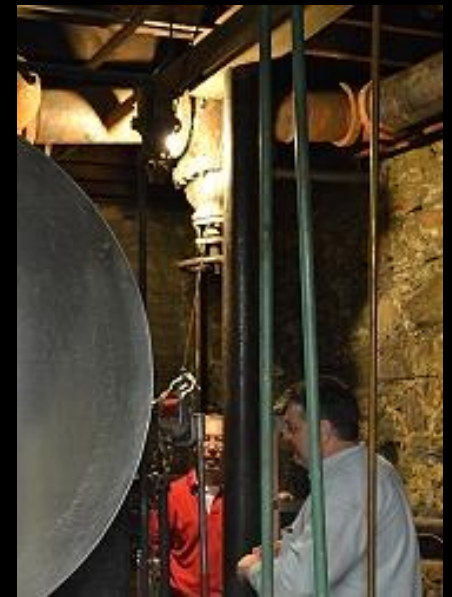



Oct 12<sup>th</sup> – tunnel framework, Ottilia steam valve, steam pipe capped off at boilers, plumbing and electrical removal





**Oct. 12<sup>th</sup> – 3<sup>rd</sup>  
and 2<sup>nd</sup> Ottilia  
demolition and  
fixture removal**





**Oct 13<sup>th</sup> – Rerouting power to Otilia, tossing the radiators, planning cuts for sewer pipes, surveying the land slope for drainage**



Oct 13<sup>th</sup> – Cutting passageway wall  
for a clean separation; 3<sup>rd</sup> Ottilia  
hallway without closets





Oct. 13<sup>th</sup> – 3<sup>rd</sup> Otilia West rooms opened back up



**Oct. 13<sup>th</sup> – 3<sup>rd</sup> Ottilia  
northwest dormer rooms  
opened up (see chimney  
at left); north bathroom  
demolition**





**Oct. 14<sup>th</sup> – Passageway ready for demolition, auditorium ready for “surgery,” Golden worker painting their signs to make them look nicer on our lovely grounds**





**Oct. 14<sup>th</sup> – pulling out the electrical cable for recycling the copper wire; even the old Ford truck is feeling the weight of the task**
